



FLORIDA TRANSPORTATION COMMISSION MEETING

July 22, 2021

**Stacy L. Miller, PE
District Six Secretary**



LENGTH

20 Miles

COST & FUNDING

\$300 Million (Fully Funded)

CONNECTS

Florida City to Dadeland
South Metrorail Station

- Federal (33%): 100M
- State (33%): 100M
- Local (33%): 100M

PROJECT COMPONENTS

- 14 Iconic BRT Stations
- Rehabilitation of Existing Stations (16 locations, 32 shelters)
- 2 Terminal Stations
- Transit Corridor Improvements along exclusive transit right-of-way
- 2 FDOT Construction Safety Projects
- At-grade crossing gate arms at all intersections
- SW 168th St Park-and-Ride/Garage

BRT STATION RENDERING




STATUS

- ✓ TPO selection of LPA – August 2018
- ✓ FTA Award of Small Starts Grant – August 2020
- ✓ FDOT Executes PTGA for \$100 Million– Sept. 2020
- ✓ Miami-Dade County BCC Award of DB services – August 2020
- ✓ DTPW Issued NTP – February 2021
- ✓ Groundbreaking Ceremony- June 4, 2021

NEXT STEPS

- Anticipated Start of Revenue Service – Spring 2023



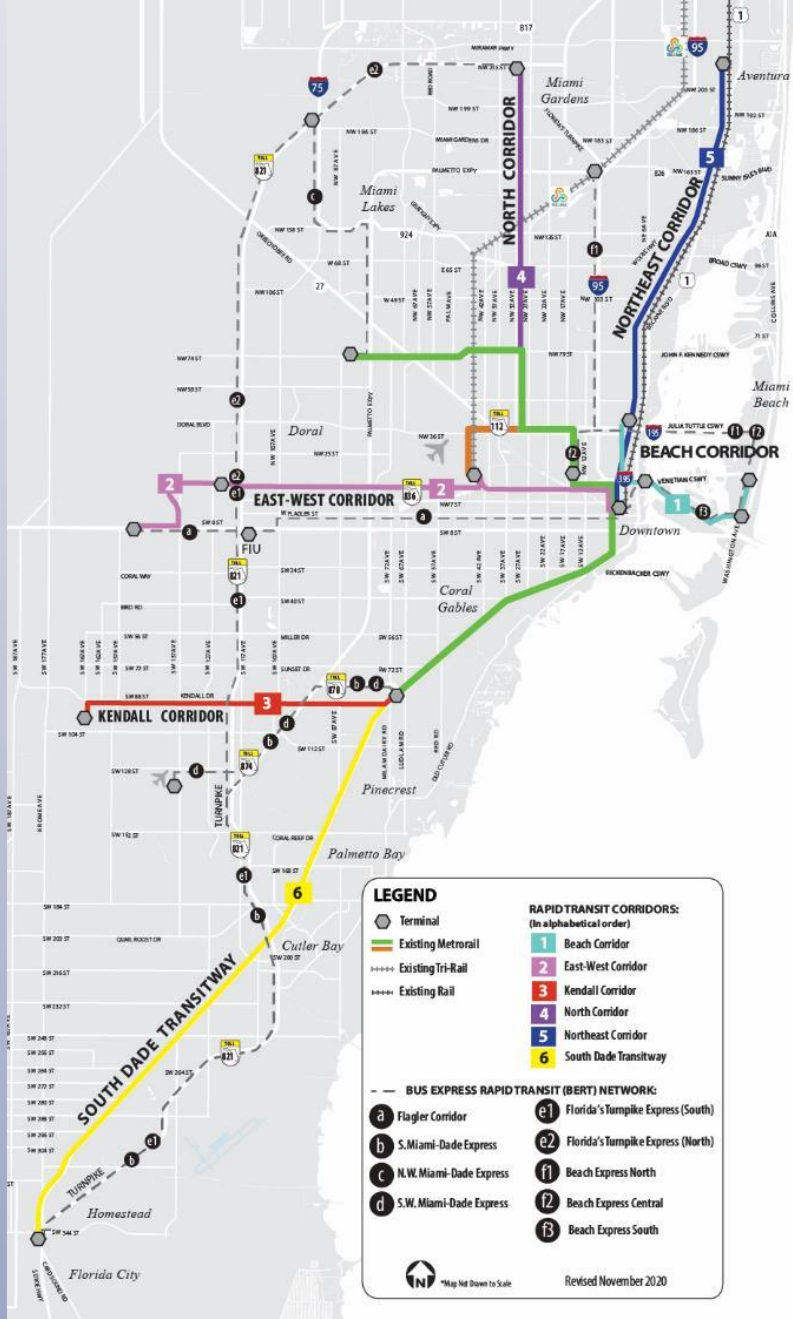

Miami-Dade County

FDOT



BEACH (Causeway Extension)

- PD&E Completion- Winter 2022
- Interim Agreement Phase- Spring 2022 (RFP track)

NORTHEAST

- Class of Action Determination-Summer 2021
- Request Entry into Project Development- Summer 2021

EAST-WEST

- Selection of LPA- October 2020
- Request Entry into Project Development- Fall 2021

NORTH¹

- PD&E Project on hold
- RFP Released by DTPW- June 2020
- Request Entry into Project Development-Summer 2022 (RFP track)

KENDALL

- Endorsement of Recommended Alternative by TPO- Fall 2021
- PD&E Completion- Winter 2023

FLAGLER (BERT Route)

- Selection of LPA- December 2021
- PD&E Completion- Fall 2022

1) PD&E study is being led by FDOT, RFP process being led by Miami-Dade County



I-395/SR 836/I-95 DESIGN-BUILD PROJECT

Financial Project Numbers: 251688-1-52-01, 423126-1-52-01, 423126-2-52-01, 429300-2-52-01



ONGOING CONSTRUCTION ACTIVITIES



- Ongoing bridge approach slab replacement
- Intelligent Transportation Systems installation
- Ongoing diamond grinding
- Concrete pavement replacement over 90% complete



Bridge approach slab replacement



ONGOING CONSTRUCTION ACTIVITIES



6-26-2021







ONGOING AND UPCOMING CONSTRUCTION ACTIVITIES

ARCH FOUNDATION CONSTRUCTION

Arches 4 and 5 ACPs completed.
Ongoing excavation of Arch 4 foundation
Ongoing construction of rebar cage for the center pier footer

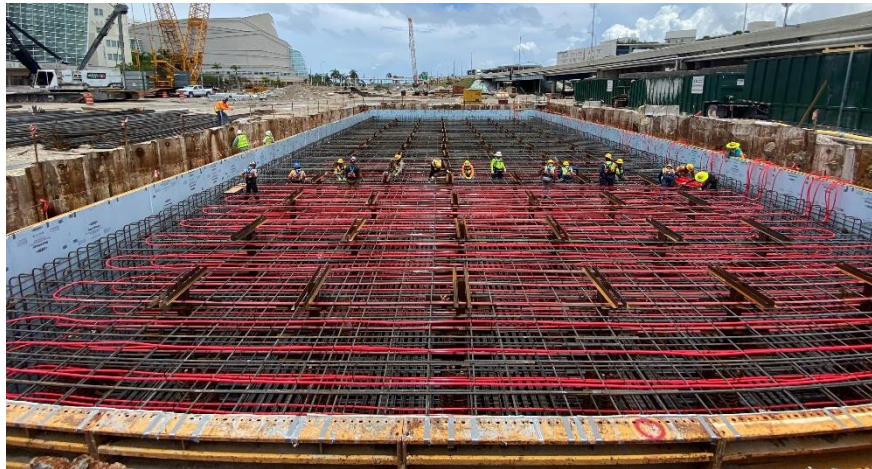

Footer construction at Arches 1 and 2.
Ongoing installation of rebar at Arch 2

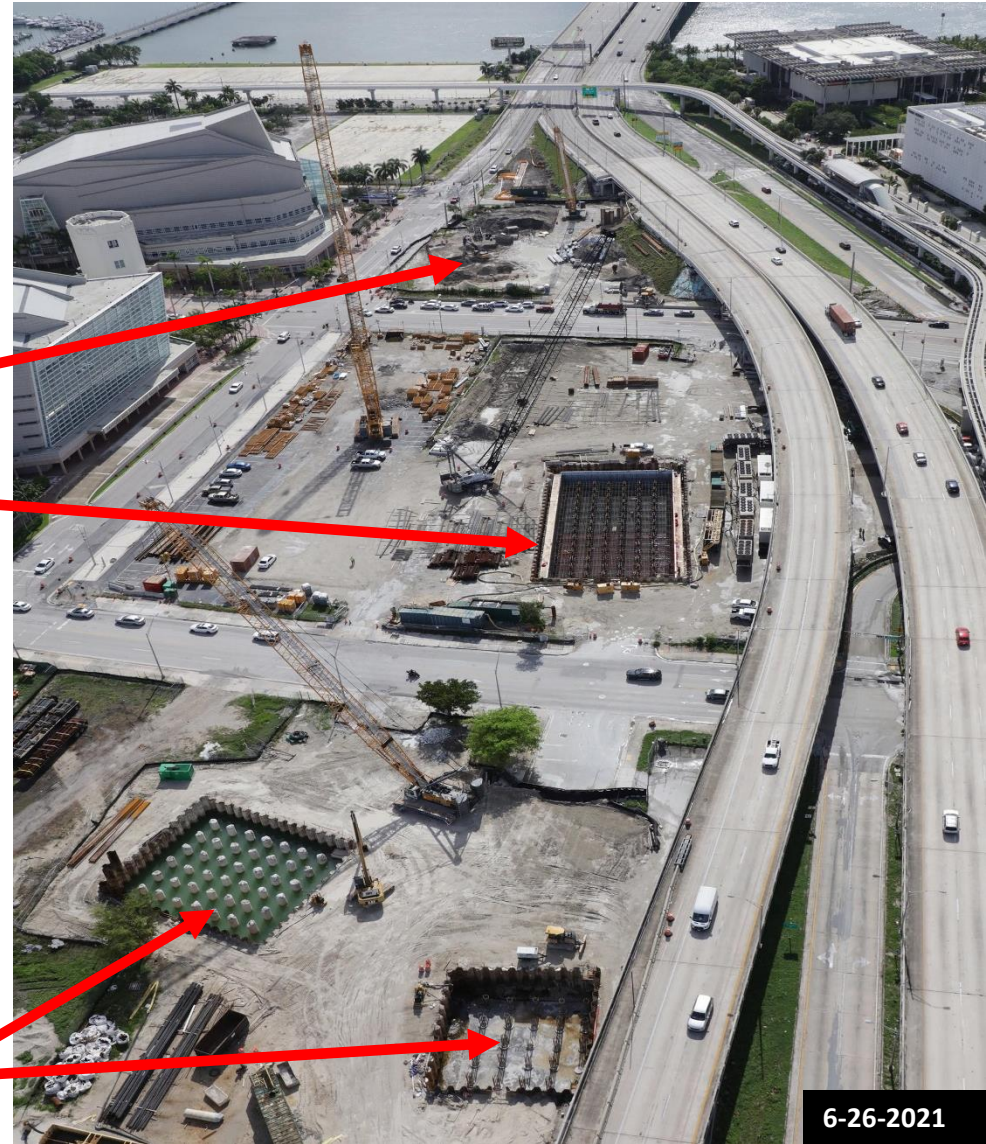

6-26-2021



ONGOING AND UPCOMING CONSTRUCTION ACTIVITIES



6-26-2021





**WHEN CROSSING THE STREET,
ALWAYS LOOK BOTH WAYS.**

fdotmiamidade.com/alerttodayflorida

